**EnvironmSafe for Engineering, Trading & Services Ltd.**
www.environmsafe.com | support@environmsafe.com
+967 78 340 2932 | Al Buraiqah, Aden, Yemen

| | | | |
|---|---|---|---|
| **Client** | DEMO – Sample Process Plant (not a real client) | **Contract / PO** | DEMO-PC0001 |
| **Project** | Demo boiler shutdown inspection | **Site** | Demo Utilities Area |
| **Report number** | ES/DEMO-PC0001-DPR-003 | **Date** | 09 Oct 2026 |
| **Day** | 3 | **Hours worked** | 20 |

## 1. MANPOWER AND HOURS

| Role | Number |
|---|---|
| Inspector | 1 |
| NDT technician | 1 |
| Helper | 2 |
| Total | 4 |

Toolbox talk: Pressure testing safety

## 2. HSE

| Lost time injuries | First aid cases | Near misses |
|---|---|---|
| 0 | 0 | 0 |

## 3. ACTIVITIES COMPLETED

| No. | Discipline | Activity completed |
|---|---|---|
| 1 | PSV | As-found tests of PSV-101A, 21-PSV-003-2, PSV 18 111-1 |
| 2 | NDT | UT survey of V-201 completed (5 CMLs) |

## 4. PROGRESS

| Planned (%) | Actual (%) | Variance (%) |
|---|---|---|
| 50 | 45 | -5 |

## 5. HOLDS AND OBSERVATIONS

| Ref. | Type | Description | Raised | Status |
|---|---|---|---|---|
| H-01 | Hold | Boiler internal access – Gas-free certificate required before drum entry. | 08 Oct 2026 | Open |
| O-01 | Observation | Scaffold tag missing at drum level | 08 Oct 2026 | Closed 09 Oct 2026 |

## 6. PLANNED ACTIVITIES – NEXT DAY

- PSV overhaul and as-left tests
- UT of P-301


*Confidential - EnvironmSafe & DEMO – Sample Process Plant (not a real client)*

**EnvironmSafe for Engineering, Trading & Services Ltd.**
www.environmsafe.com | support@environmsafe.com
+967 78 340 2932 | Al Buraiqah, Aden, Yemen

## 7. ISSUES AND CONSTRAINTS

Gas-free certificate for drum entry still awaited (H-01).

## 8. PHOTOGRAPHS

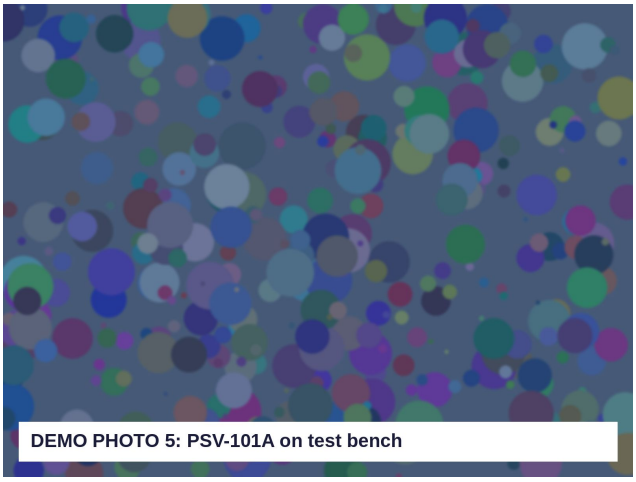



**Figure 1 –** PSV-101A on the test bench





**Figure 2 –** Boiler B-101 front

| Prepared by | Client representative |
|---|---|
| **Demo Inspector**<br>Date: 09 Oct 2026 | Date: |
